



DRAFT, SUBJECT TO REVISION - June 4, 2018
Updates to the Coordinated Long-term Operation of the CVP and SWP DRAFT Schedule

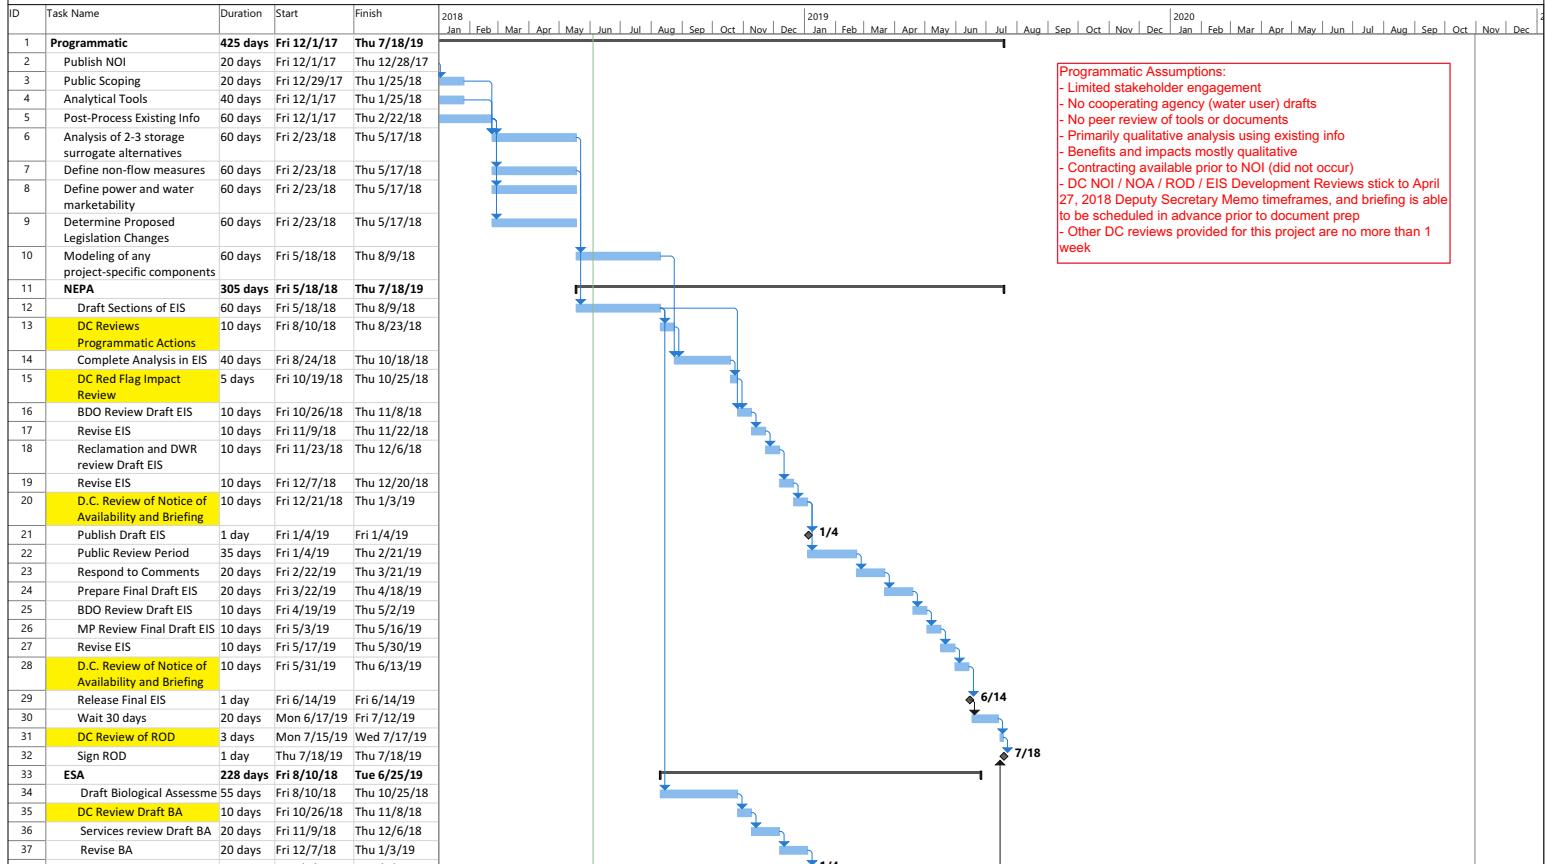

DRAFT, SUBJECT TO REVISION - June 4, 2018
 Updates to the Coordinated Long-term Operation of the CVP and SWP DRAFT Schedule

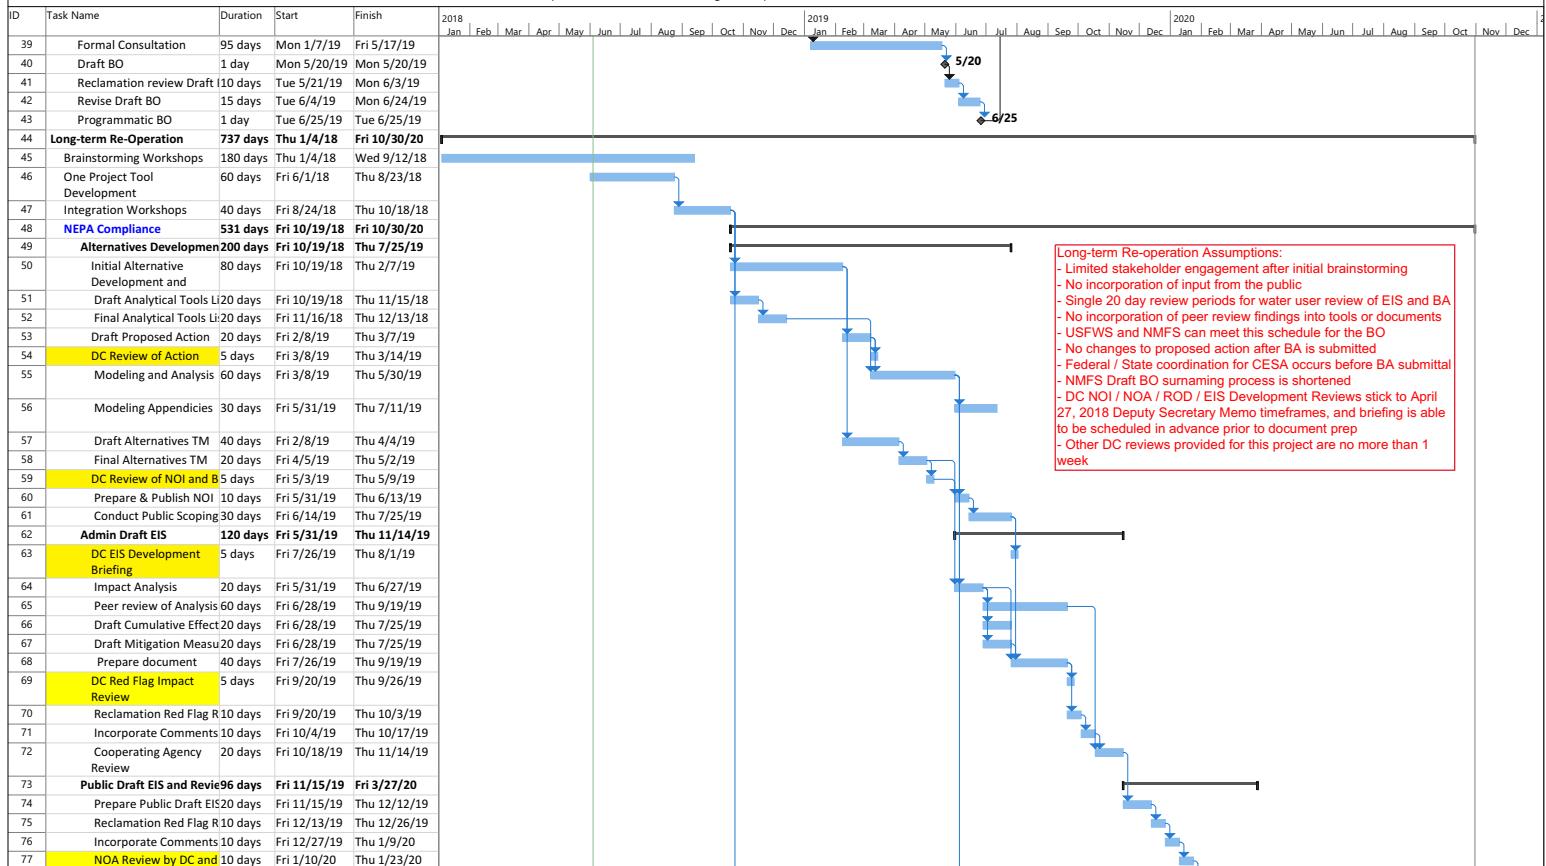

DRAFT, SUBJECT TO REVISION - June 4, 2018
Updates to the Coordinated Long-term Operation of the CVP and SWP DRAFT Schedule

The Gantt chart illustrates the timeline for the Draft Environmental Impact Statement (EIS) and Biological Assessment (BA) process. The timeline spans from January 2018 to December 2020. Key milestones include the publication of the Draft EIS in January 2020, the preparation of the Final EIS and ROD in March 2020, and the submission of the Final BA to NMFI in December 2020. The chart also highlights the NOA Review by DC and Briefing, the preparation of the Record of Decision, and the review by various agencies like DNR, DC, and DWR. The chart uses blue bars for tasks and arrows for dependencies, with specific dates marked on the timeline.

ID	Task Name	Duration	Start	Finish
78	Publish Draft EIS	1 day	Fri 1/24/20	Fri 1/24/20
79	Public Hearings on Pub130 days	Mon 1/27/20	Fri 3/6/20	
80	Public Comment Period15 days	Mon 3/9/20	Fri 3/27/20	
81	Final EIS and ROD	155 days	Mon 3/30/20	Fri 10/30/20
82	Respond to Comments 40 days	Mon 3/30/20	Fri 5/22/20	
83	Prepare Final EIS	40 days	Mon 5/25/20	Fri 7/17/20
84	Reclamation Review	10 days	Mon 7/20/20	Fri 7/31/20
85	Incorporate Comments 20 days	Mon 8/3/20	Fri 8/28/20	
86	NOA Review by DC and Briefing	10 days	Mon 8/31/20	Fri 9/11/20
87	Publish Final EIS	1 day	Mon 9/14/20	Mon 9/14/20
88	Wait 30 days	20 days	Tue 9/15/20	Mon 10/12/20
89	Prepare Record of Deci	10 days	Tue 10/13/20	Mon 10/26/20
90	DC Review of ROD	3 days	Tue 10/27/20	Thu 10/29/20
91	Sign Record of Decision	1 day	Fri 10/30/20	Fri 10/30/20
92	Endangered Species Act Com	482 days	Fri 10/19/18	Mon 8/24/20
93	Admin Draft BA	265 days	Fri 10/19/18	Thu 10/24/19
94	Draft Introductory Sect	30 days	Fri 10/19/18	Thu 11/29/18
95	Draft Species Accounts	30 days	Fri 11/30/18	Thu 1/10/19
96	Effects Analysis	20 days	Fri 5/31/19	Thu 6/27/19
97	Peer Review of Effects	60 days	Fri 6/28/19	Thu 9/19/19
98	Prepare Admin Draft BA	20 days	Fri 6/28/19	Thu 7/25/19
99	DC Review, Reclamation and DWR Review of Draft BA	5 days	Fri 7/26/19	Thu 8/1/19
100	Incorporate Comments	10 days	Fri 8/2/19	Thu 8/15/19
101	Agency Review	10 days	Fri 8/16/19	Thu 8/29/19
102	Incorporate Comments	20 days	Fri 8/30/19	Thu 9/26/19
103	DNFR Review	20 days	Fri 9/27/19	Thu 10/24/19
104	Final BA	41 days	Fri 10/25/19	Fri 12/20/19
105	Prepare Final BA	20 days	Fri 10/25/19	Thu 11/21/19
106	DC, Reclamation, and DWR Review	10 days	Fri 11/22/19	Thu 12/5/19
107	Incorporate Comments	10 days	Fri 12/6/19	Thu 12/19/19
108	Submit Final BA to NMFI	1 day	Fri 12/20/19	Fri 12/20/19
109	Biological Opinions	176 days	Mon 12/23/19	Mon 8/24/20
110	Draft BOs	95 days	Mon 12/23/19	Fri 5/1/20
111	DC, Reclamation, and Water User Review of Draft BO	20 days	Mon 5/4/20	Fri 5/29/20
112	Peer Review of BO	60 days	Mon 5/4/20	Fri 7/24/20
113	Revise BO Based on Coro	60 days	Mon 6/1/20	Fri 8/21/20
114	Submit Final BO's to Re	1 day	Mon 8/24/20	Mon 8/24/20
